

MAADEN ARGP

Digitalization Platform

Internal Management Briefing

What we are bidding for, who the client is, the scope, the team, the timeline, and the price

Executive Summary

In one slide - what is this opportunity?

CLIENT

Maaden

Saudi Arabian Mining Company (KSA national flagship)

PROJECT

ARGP

Ar Rjum Gold Project - greenfield mining megaproject

YEAR 1 PRICE

AED 2.98M

AUD 1.1M / USD 812K (incl WHT)

5-YEAR TCO

AED 4.91M

Y1 + 4 years maintenance

WHAT WE ARE BIDDING FOR

Design, build, deploy and hand over a custom Digitalization Platform for the ARGP gold project - a 12-month engagement covering 5 functional modules + AI agents + KSA in-Kingdom hosting + 24/7 SLA.

WHY THIS MATTERS

1

Strategic Win

First major KSA enterprise platform deal. Opens door to Aramco, SABIC, ADNOC follow-ons.

2

Low Y1 Cash

AED 2.98M Y1 vs incumbents at AED 80-150M - we win on price + flexibility.

3

Tight Margin

35% gross margin. Manage scope creep tightly via Variation Clause 4.

The Client and the Project

Who is Maaden and what is ARGP?

THE CLIENT - MAADEN

Saudi Arabian Mining Company

Publicly traded - HQ Riyadh, KSA
Largest mining company in Middle East
Government-aligned (PIF-owned majority)
Saudi Vision 2030 cornerstone enterprise

Affiliates (this scope: ARGP only):

- Maaden Aluminium
- Maaden Phosphate Company (MPC)
- **Ar Rjum Gold Project (ARGP)**
- Multiple gold & industrial operations

THE PROJECT - ARGP

Ar Rjum Gold Project

Flagship greenfield gold mining + processing
Multi-year mining megaproject (Ras Al-Khair)
Scale: USD-billions project budget
Vision 2030: local content + supply chain

What Maaden tendered:

SoW: ARGP-DIGI-APP-SOW-001 Rev. 00
Date: 02 April 2025
AI-powered enterprise platform
KSA in-Kingdom data residency required

Note: ARGP is the first affiliate. Multi-affiliate rollout is excluded from this scope (variation per affiliate).

What Maaden Is Asking For

5 functional modules + AI capabilities + KSA hosting + compliance

M1 Engineering & Design Management

CDE + AI design checks + Digital Twin + 20 disciplines + Aconex integration

M2 Schedule Management & Project Controls

Primavera P6 + QSRA + EVMS + AWP + look-ahead

M3 Construction & Pre-Commissioning

8 sub-modules + AWP + Punch List + Pre-Comm + Computer Vision

M4 Quality Management & Assurance

Digital ITPs + NCR + CAPA + supplier scorecards + AI predictive quality

M5 Procurement & Supply Chain

PO + Material Traceability + EAC + integrated with ERP

CROSS-CUTTING

AI / ML Engine

Predictive analytics, CV, QSRA

KSA In-Kingdom Hosting

Azure Riyadh / Oracle KSA

Compliance

NCA ECC + PDPL + CCRF + ISO

WHY THIS PROPOSAL IS COMPLEX

- 5 separate modules each with their own SoW sections (3.1, 3.2, 3.3, 3.4, 3.5)
- Mandates AI capabilities (predictive analytics, CV, Digital Twin, QSRA)
- Mandates KSA data residency + integration with 6+ Maaden enterprise systems (Aconex, P6, SAP, Aveva PI, MS EPM, ADFS, SIEM)
- 4-phase delivery with gate reviews at Weeks 4, 12, 16, 52

Our Delivery Approach

4 phases over 12 months per SoW 3.3.10 + ongoing Year 2-5 maintenance

PHASE 1 W 1-4	PHASE 2 W 5-12	PHASE 3 W 13-16	PHASE 4 W 17-52
Setup & Mobilisation	Pilot Module Deployment	Pilot Validation + Training	Full Rollout + IP Transfer
- Project kickoff - BIM Execution Plan - KSA tenant on Maaden cloud - Maaden AAD / ADFS SSO setup - NCA ECC + PDPL baseline - Architecture design - Requirements workshops	- Module 3 AWP pilot build - 4 AI agents (ingest, ontology, anomaly, KPI synthesiser) - Aconex + P6 integrations - 5 pilot dashboards - Test pack + UAT prep	- UAT on Maaden data - KPI measurement vs targets - Defect triage + fixes - Train-the-trainer (8 modules) - Phase 3 acceptance gate	- Build Modules M1, M2, M4, M5 - SAP + Aveva PI + EPM integration - Multi-area ARGP rollout - Security hardening + audit - Go-Live + Final Acceptance - 1-month hyper-care
AED 232.7K	AED 625.7K	AED 269.8K	AED 1.71M

YEAR 2-5: ANNUAL MAINTENANCE & SUPPORT

Annual maintenance fee = 15% of build cost base, escalated 5% per year

Includes: bug fixes, security patches, minor enhancements, user support, 24/7 SLA per SoW 3.3.10

Y2 AED 426K | Y3 AED 447K | Y4 AED 469K | Y5 AED 490K

Total Y2-5 NET (excl WHT): AED 1,832,525 || 5-YEAR TCO: AED 4,907,333 (incl WHT)

Gate Reviews at end of each phase let Maaden exit if expectations not met - reduces our delivery risk

The Team

7 unique roles deployed across the 4 phases (SoW 3.4.7 mandatory + necessary)

Programme Manager

SOW 3.4.7 mandated

Deployment: M1-M12

Single point of contact, gate reviews, Maaden steering

Solution Architect

SOW 3.4.7 Sr Functional/Technical

Deployment: M1-M12

Platform + integration architecture, code reviews, IP design

Senior Database Administrator

SOW 3.4.7 mandated

Deployment: M1-M12 (0.5 in M1)

DB schema, performance, backup + DR

Documents Controller

SOW 3.4.7 mandated

Deployment: M1-M12

Document control, transmittals, evidence pack

KSA Compliance / Security Lead

SOW 3.4.4 mandatory

Deployment: M1-M12

NCA ECC + PDPL + CCRF compliance, SIEM integration

AI / ML Engineer

SOW 3.3.4 - delivery of AI

Deployment: M2-M12

4 production AI agents trained on Maaden data

Module Specialist

SOW 3.3.4 - module build

Deployment: M2-M12

Builds 5 modules from scratch

TEAM SUMMARY

7 unique roles

Peak: 5.5 FTE (Phase 1)

Avg: 4 FTE across 12 months

Total Y1: ~33 FTE-months

Mix: 40% Onsite RAK
60% Offsite Dubai


Year 2-5 Run Team:

2-3 FTE shared pool

Lean post-handover support

Timeline

52-week programme from PO + Y2-5 maintenance window

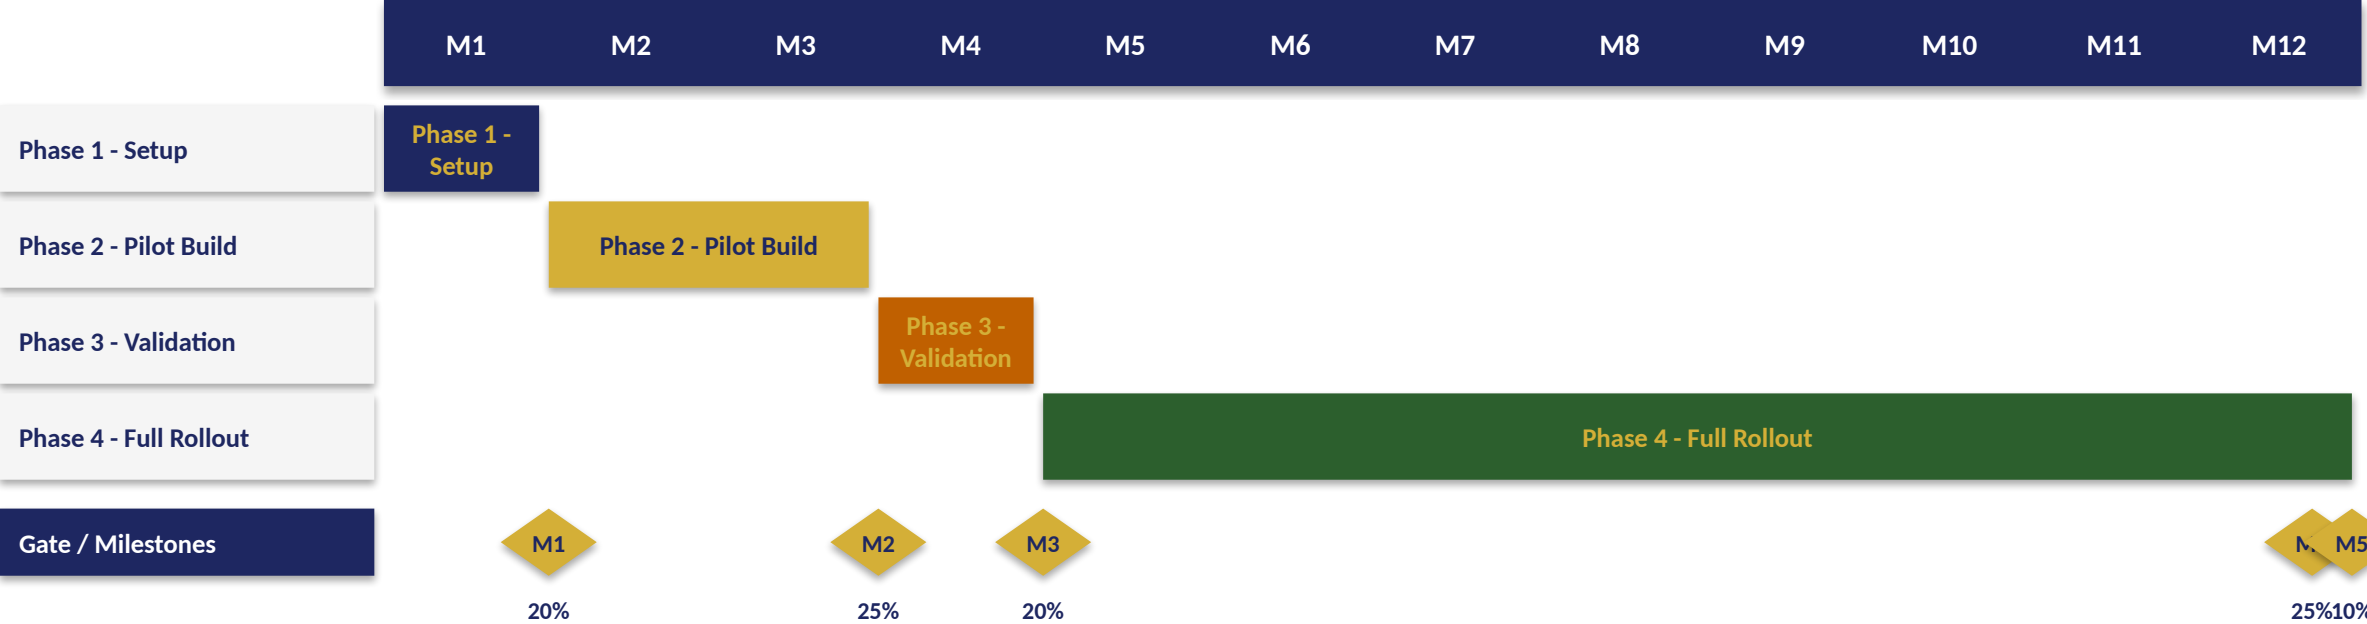

Payment Milestones: M1 Phase 1 mob | M2 Pilot Acceptance | M3 KPI Gate | M4 Go-Live + IP Transfer | M5 Hyper-care Exit

Year 2 - Year 5: Annual Maintenance Contract (renewable at each anniversary)

KEY DATES

Contract effective date:	TBC (assumes within 90 days of bid)
Phase 1 Mobilisation:	Week 4 (end Month 1)
Phase 2 Pilot Live:	Week 12 (end Month 3)
Phase 3 KPI Gate:	Week 16 (end Month 4)
Go-Live + IP Transfer + Final Acceptance:	Week 52 (end Month 12)

Commercials

Year 1 price + 5-Year Total Cost of Ownership for Maaden

YEAR 1 - TOTAL PRICE

AED 2.98M

Build Fees: AED 2,841,125
5% KSA WHT: AED 142,056
TOTAL inc WHT: AED 2,983,181
USD 812K | AUD 1.16M | SAR 3.04M

5-YEAR TCO TO MAADEN

AED 4.91M

Y1 Build: AED 2.98M
Y2-5 Maintenance: AED 1.92M
TOTAL 5-YR TCO: AED 4,907,333
USD 1.34M (excl any rollout variations)

PHASE FEE BREAKDOWN (Year 1, ex WHT)

Phase 1	Setup + Mobilisation	W 1-4	AED 232,687.50
Phase 2	Pilot Module Deployment	W 5-12	AED 625,685.00
Phase 3	Pilot Validation + Training	W 13-16	AED 269,832.50
Phase 4	Full Rollout + IP Transfer	W 17-52	AED 1,712,920.00
YEAR 1 BUILD FEES SUBTOTAL			AED 2,841,125

VS COMPETITION | Bentley iTwin: SAR 90-130M 5-Yr | Cohesive: 100-150M | Hexagon: 95-140M | XDH: SAR 5M

Pricing is in AED. Bank account AED (UAE). Payment terms 20% mobilisation + 70% progress + 10% acceptance.

Risks & Open Clarifications

10 must-ask questions and how we are protected if Maaden does not answer

TOP 10 - MUST-ASK BEFORE BID SUBMISSION

- A.1** Implementation duration - SoW says "XX months" - blank
- A.2** Phase 4 end date - "Weeks 17+" open-ended
- B.1** Module timeline conflict - 8 weeks vs 17 weeks across SoW sections
- B.4** Master sequencing of 5 modules in Year 1 vs Year 2
- L.1** Is this ONE bidder or TWO (SoW has 2 vendor sections)?
- N.6** Is UAE-incorporated XDH acceptable as Prime?
- I.1** Currency - AED, SAR, USD?
- E.1** How many users?
- E.2** How much data (TB)?
- D.1** Which KSA cloud provider preferred?

HOW WE ARE PROTECTED

Stated XDH Assumption for each item

If Maaden does not answer, our assumption defines bid scope

Variation Clause 4 in T&C

Scope change = re-priced under Change Order procedure

Phase Gate Reviews

Maaden can exit at end of each phase - limits our delivery risk

Excluded items list (Section 7)

Maaden direct procurement:
AI APIs / Hosting / GPU /
3rd-party SW / Hardware
Indicative ~SAR 40-55M over 5y

Our Strategic Position

Why this is winnable, and what we need to do next

1. Land at low price

Maaden has not bought from a UAE small/mid vendor before. We win on:

- AED 2.98M Y1 vs SAR 25-50M from Bentley/Cohesive/Hexagon
- 7-person lean team
- Flexible phase-gate commercial structure

2. Prove value at Pilot

Phase 2 (Weeks 5-12) is where we prove capability:

- Module 3 AWP working on real ARGP data
- 4 production AI agents trained on Maaden data
- 5 KPI dashboards vs SoW Section 4 targets
- Acceptance gate W12

3. Expand into Year 2+

Once Y1 lands, expand via:

- M5 Procurement production (Y2 variation)
- Module 4 Phase 2 quality features
- Additional Maaden affiliates
- New CV / Digital Twin scope
- Multi-year recurring maintenance

NEXT STEPS

1. **Finalise the 4-file bid pack (Letter, PC, Manpower, PD) - 90% complete**
2. Fill Maaden Pricing Structure Template in their format - 1 day work
3. Issue formal RFI with 60-item clarification list (with XDH assumptions for protection)
4. Internal sign-off from CEO + CFO on commercial terms (margin, payment, retention)
5. **Submit bid to Maaden procurement via MS EPM (per SoW 3.4.7)**
6. Prepare for resource interviews (SoW 3.4.7 mandates Maaden interviews proposed team)
